
Nottingham Ring Road Improvement Scheme - Crown Island

Phase 4

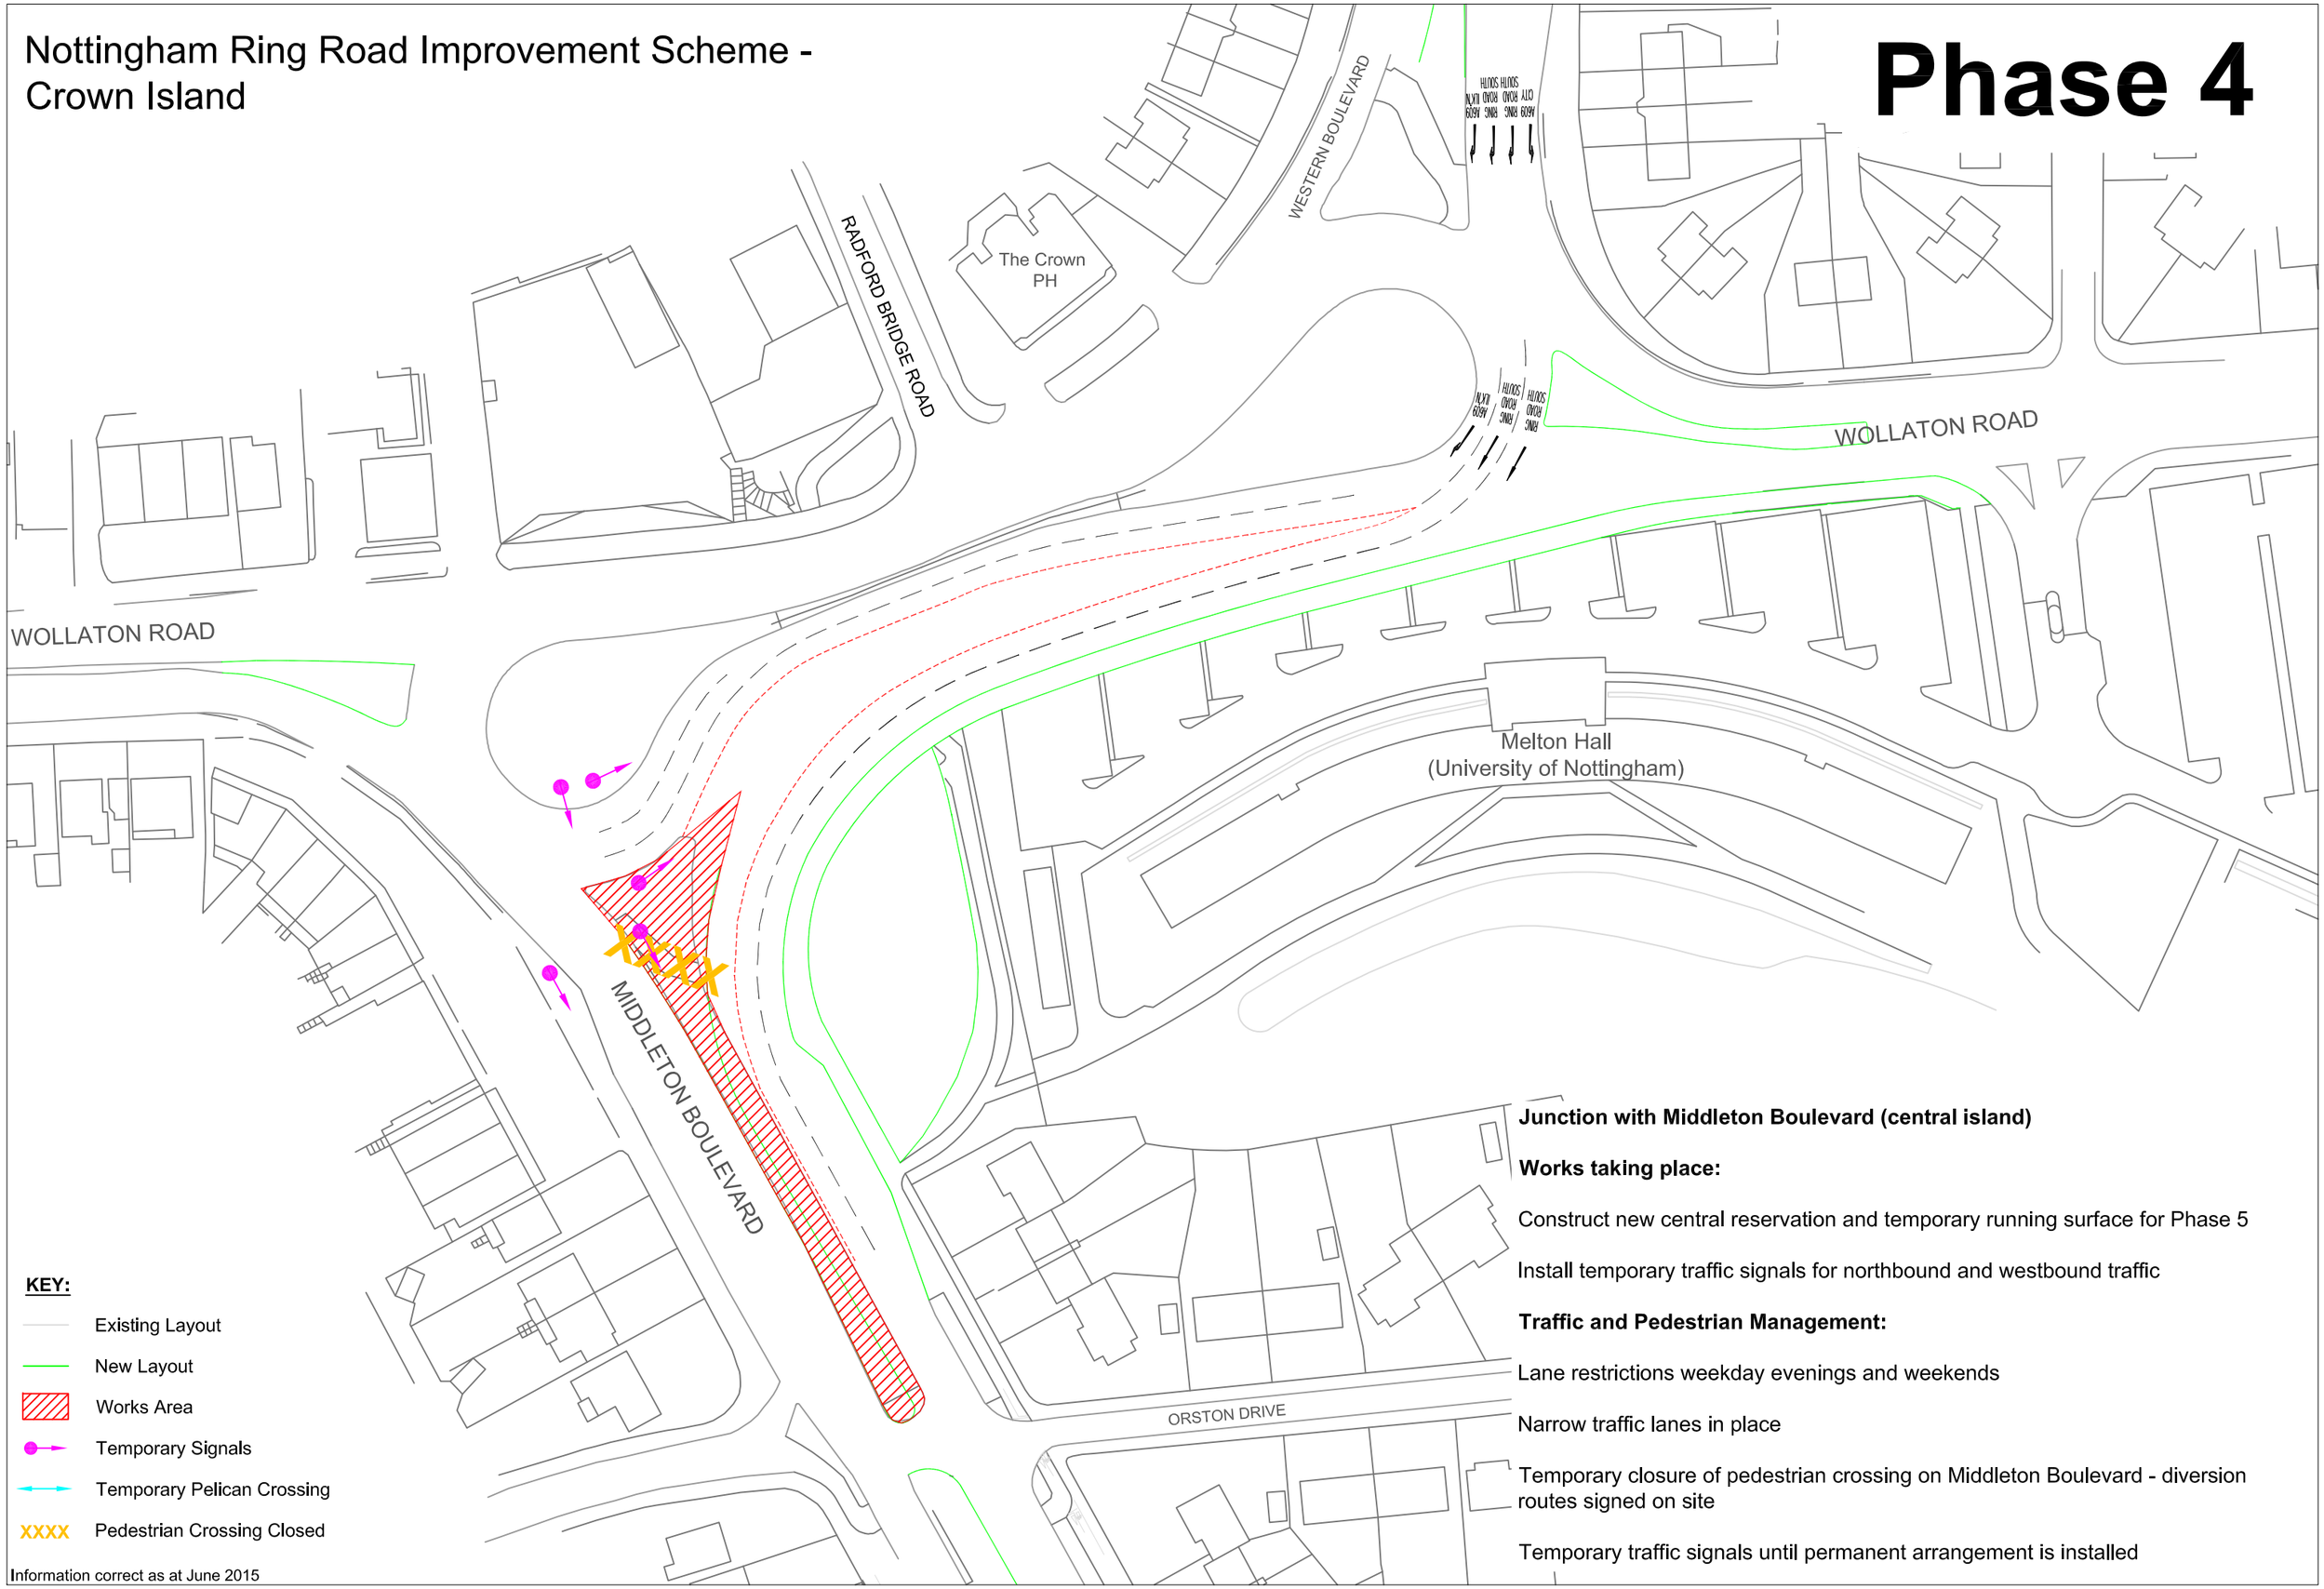

KEY:

- Existing Layout
- New Layout
- Works Area
- Temporary Signals
- Temporary Pelican Crossing
- XXXX Pedestrian Crossing Closed

Information correct as at June 2015

Junction with Middleton Boulevard (central island)

Works taking place:

Construct new central reservation and temporary running surface for Phase 5

Install temporary traffic signals for northbound and westbound traffic

Traffic and Pedestrian Management:

Lane restrictions weekday evenings and weekends

Narrow traffic lanes in place

Temporary closure of pedestrian crossing on Middleton Boulevard - diversion routes signed on site

Temporary traffic signals until permanent arrangement is installed
